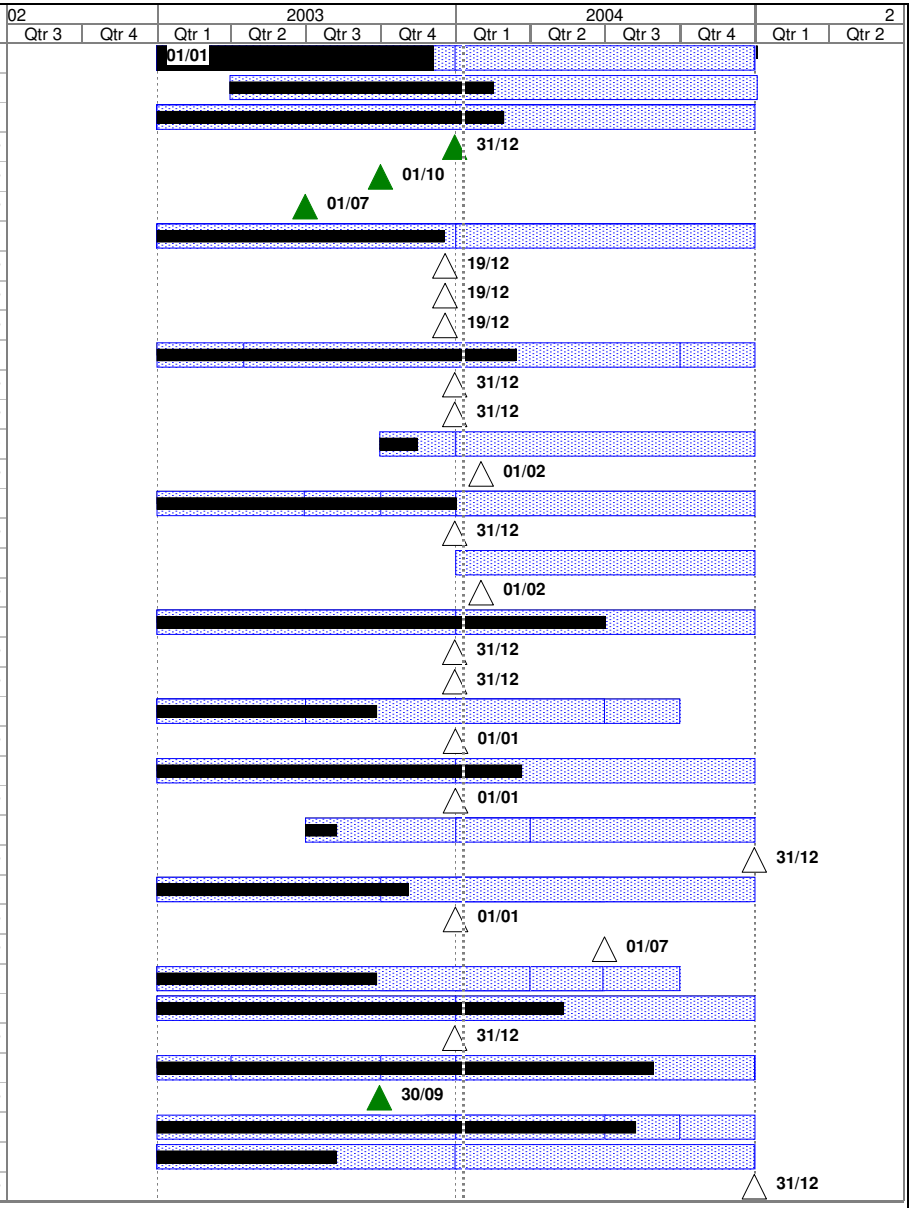ID	WP	Task Name	Start	Finish	% Comp.
0	**0**	**vdfs_prog_20040109**	**Wed 01/01/03**	**Mon 03/01/05**	**46%**
1		**Quarterly Reviews**	**Mon 31/03/03**	**Mon 03/01/05**	**50%**
10	**1**	**Management and Defenition of Responsibilities**	**Wed 01/01/03**	**Fri 31/12/04**	**58%**
20	D1a	ICD between CASU and JAC	Wed 31/12/03	Wed 31/12/03	100%
21	D1b	ICD between CASU and WFAU	Wed 01/10/03	Wed 01/10/03	100%
22	D1c	Fits headers and data structures defention document	Tue 01/07/03	Tue 01/07/03	100%
23	**2**	**ESO VISTA software deliverables and documentation**	**Wed 01/01/03**	**Fri 31/12/04**	**48%**
33	D2a	Calibration plan document	Fri 19/12/03	Fri 19/12/03	0%
34	D2b	Data Interface Dictionary	Fri 19/12/03	Fri 19/12/03	0%
35	D2c	DFS user requirements document	Fri 19/12/03	Fri 19/12/03	0%
36	**3**	**Pipeline Infrastructure and Progress Monitoring Tools**	**Wed 01/01/03**	**Fri 31/12/04**	**60%**
44	D3a	Deliver pipeline V1.0	Wed 31/12/03	Wed 31/12/03	0%
45	D3b	Deliver documentation for pipeline V1.0	Wed 31/12/03	Wed 31/12/03	0%
46	**4**	**Set up and Manage Raw Science Archive**	**Tue 30/09/03**	**Fri 31/12/04**	**10%**
49	D4a	Create Raw Science Archive	Sun 01/02/04	Mon 02/02/04	0%
50	**5**	**Set up and Manage Data Processing System Hardware**	**Wed 01/01/03**	**Fri 31/12/04**	**50%**
56	D5a	Processing hardware in place	Wed 31/12/03	Wed 31/12/03	0%
57	**6**	**Run Standard Pipeline**	**Thu 01/01/04**	**Fri 31/12/04**	**0%**
66	D6a	Data flow to WFAU initiated	Sun 01/02/04	Mon 02/02/04	0%
67	**7**	**Development Work for Summit Pipeline**	**Wed 01/01/03**	**Fri 31/12/04**	**75%**
72	D7a	Deliver summit pipeline	Wed 31/12/03	Wed 31/12/03	0%
73	D7b	Deliver summit pipeline documentation	Wed 31/12/03	Wed 31/12/03	0%
74	**8**	**Development and Testing of Standard 2D Processing**	**Wed 01/01/03**	**Thu 30/09/04**	**42%**
82	D8a	Complete 2D processing modules V1.0	Thu 01/01/04	Thu 01/01/04	0%
83	**9**	**Development and Testing of Standard Catalogue Products**	**Wed 01/01/03**	**Fri 31/12/04**	**61%**
91	D9a	Complete standard catalogue modules V1.0	Thu 01/01/04	Thu 01/01/04	0%
92	**10**	**Set Up, Trial and Run Further Processing Software**	**Tue 01/07/03**	**Fri 31/12/04**	**7%**
100	D10a	Deliver 2D PSF and Sersic fitting applications	Fri 31/12/04	Fri 31/12/04	0%
101	**11**	**Photometric Standards and Calibraion**	**Wed 01/01/03**	**Fri 31/12/04**	**42%**
109	D11a	Allocate primary and secondary standard stars/fields	Thu 01/01/04	Thu 01/07/04	0%
110	D11b	Photometric calibration and colour equations	Thu 01/07/04	Thu 01/07/04	0%
111	**12**	**Further Development of DQC Measures**	**Wed 01/01/03**	**Thu 30/09/04**	**42%**
116	**13**	**Co-located List Driven Photometry**	**Wed 01/01/03**	**Fri 31/12/04**	**68%**
120	D13a	Deliver list driven photometer	Wed 31/12/03	Wed 31/12/03	0%
121	**14**	**Stacking and Mosaicing**	**Wed 01/01/03**	**Fri 31/12/04**	**83%**
127	D14	Deliver basic stacker and mosaicer	Tue 30/09/03	Tue 30/09/03	100%
128	**15**	**Continuum Subtraction and Basic Difference Imaging**	**Wed 01/01/03**	**Fri 31/12/04**	**80%**
133	**16**	**Interpolation Techniques and PSF Modelling**	**Wed 01/01/03**	**Fri 31/12/04**	**30%**
139	D16a	Deliver PSF photometer	Fri 31/12/04	Fri 31/12/04	0%
