ID	WBS	% Work Cor	Task Name	Staff	Work	Start	Finish	Predecessors	Successors	Duration
1	**1**	**4%**	**VDFS**	**5.57**	**232 mons**	**01 Oct '04**	**30 Sep '07**			**41.65 mons**
2	**1.1**	**0%**	**Milestones - ESO**	**0**	**0 mons**	**24 Jan '05**	**20 Oct '06**			**24.21 mons**
3	1.1.1	0%	VDFS FDR @ ESO	0	0 mons	24 Jan '05	24 Jan '05	17,27,20	18,28,33,21	0 days
4	1.1.2	0%	VIRCAM Pre. Acc. Europe	0	0 mons	19 Jan '06	19 Jan '06	22	23	0 days
5	1.1.3	0%	VIRCAM COMmissioning	0	0 mons	01 Jun '06	01 Jun '06	18,24	29,25	0 days
6	1.1.4	0%	VISTA Pre. Acc. Chile	0	0 mons	20 Oct '06	20 Oct '06	25,29		0 days
7	**1.2**	**0%**	**Milestones - UK**	**0**	**0 mons**	**21 Jun '05**	**30 Sep '07**			**31.65 mons**
8	1.2.1	0%	VDFS v2 (WFcam)	0	0 mons	21 Jun '05	21 Jun '05	31,37		0 mons
9	1.2.2	0%	UK FDR	0	0 mons	16 Sep '05	16 Sep '05	33,39	34,40	0 days
10	1.2.3	0%	VDFS v3 (WFcam)	0	0 mons	20 Dec '05	20 Dec '05	32,38		0 days
11	1.2.4	0%	VDFS v4 (VISTA)	0	0 mons	20 Dec '06	20 Dec '06	34,40		0 days
12	1.2.5	0%	VDFS v5 (VISTA)	0	0 mons	30 Sep '07	30 Sep '07	35,41		0 days
13	**1.3**	**0%**	**External Dependencies**	**0**	**0 mons**	**29 Jul '05**	**29 Jul '05**			**0 mons**
14	1.3.1	0%	VIRCAM simulated data	0	0 mons	29 Jul '05	29 Jul '05		21FF+1 mon	0 mons
15	**1.4**	**13%**	**ESO deliverables**	**2.14**	**55 mons**	**01 Oct '04**	**04 Aug '06**			**25.65 mons**
16	**1.4.1**	**38%**	**Calibration Plan**	**0.25**	**4 mons**	**01 Oct '04**	**28 Nov '05**			**16.07 mons**
17	1.4.1.1	75%	v0.1 to v0.5	0.67	2 mons	01 Oct '04	20 Dec '04		18,3	60 days
18	1.4.1.2	0%	v0.5 to v1.0	0.17	2 mons	24 Jan '05	28 Nov '05	17,3	5	235 days
19	**1.4.2**	**11%**	**Data Reduction Library**	**1.83**	**47 mons**	**01 Oct '04**	**04 Aug '06**			**25.65 mons**
20	1.4.2.1	100%	DRL Design v1.0	1.67	5 mons	01 Oct '04	20 Dec '04		3	60 days
21	1.4.2.2	0%	DRL prototype	2.3	20 mons	24 Jan '05	08 Sep '05	,14FF+1 mon	22	174 days
22	1.4.2.3	0%	DRL v0.1++	2	10 mons	08 Sep '05	17 Jan '06	21	4,23	100.13 days
23	1.4.2.4	0%	DRL v1.0	2.4	6 mons	19 Jan '06	24 Mar '06	22,4	34,24	50 days
24	1.4.2.5	0%	Pipeline v0.8 (ESO resp.)	0	0 mons	24 Mar '06	30 May '06	23	25,5	50 days
25	1.4.2.6	0%	DRL v1.x	2.4	6 mons	01 Jun '06	04 Aug '06	5,24	6	50 days
26	**1.4.3**	**13%**	**ETC**	**0.16**	**4 mons**	**01 Oct '04**	**31 Jul '06**			**25.4 mons**
27	1.4.3.1	50%	ETC Spec. V1.0	0.33	1 mon	01 Oct '04	20 Dec '04		28,3	60 days
28	1.4.3.2	0%	ETC v1.0	0.17	2 mons	24 Jan '05	28 Nov '05	3,27	29	235 days
29	1.4.3.3	0%	ETC v1.x	0.44	1 mon	01 Jun '06	31 Jul '06	28,5	6	45 days
30	**1.5**	**3%**	**UK pipeline**	**1.05**	**40 mons**	**01 Oct '04**	**27 Jun '07**			**38.03 mons**
31	1.5.1	25%	v2 WFcam pipeline tuned with comm'g data	0.5	5 mons	01 Oct '04	21 Jun '05		8	200 days
32	1.5.2	0%	v3 WFcam pipeline enhanced	0.56	5 mons	01 Oct '04	25 May '05		10,34	180 days
33	1.5.3	0%	v4 VISTA UK pipeline design	0.65	5 mons	24 Jan '05	15 Aug '05	3	9	155 days
34	1.5.4	0%	v4 VISTA UK pipeline implementation	1.5	15 mons	24 Mar '06	13 Dec '06	32,23,9	35,11	200 days
35	1.5.5	0%	v5 VISTA UK pipeline	1.34	10 mons	13 Dec '06	27 Jun '07	34	12	149 days
36	**1.6**	**0%**	**Science Archive**	**3.3**	**137 mons**	**01 Oct '04**	**26 Sep '07**			**41.5 mons**
37	1.6.1	0%	v2 WFcam archive tuned	3.3	33 mons	01 Oct '04	21 Jun '05		38,8	200 days
38	1.6.2	0%	v3 WFcam archive final	3.26	22 mons	21 Jun '05	15 Dec '05	37	10,40	135 days
39	1.6.3	0%	v4 VISTA archive design	0.77	6 mons	24 Jan '05	15 Aug '05		40,9	155 days
40	1.6.4	0%	v4 VISTA archive implementation	2.86	40 mons	15 Dec '05	18 Dec '06	39,38,9	11,41	280 days
41	1.6.5	0%	v5 VISTA archive tuned	3.35	36 mons	18 Dec '06	26 Sep '07	40	12	215 days

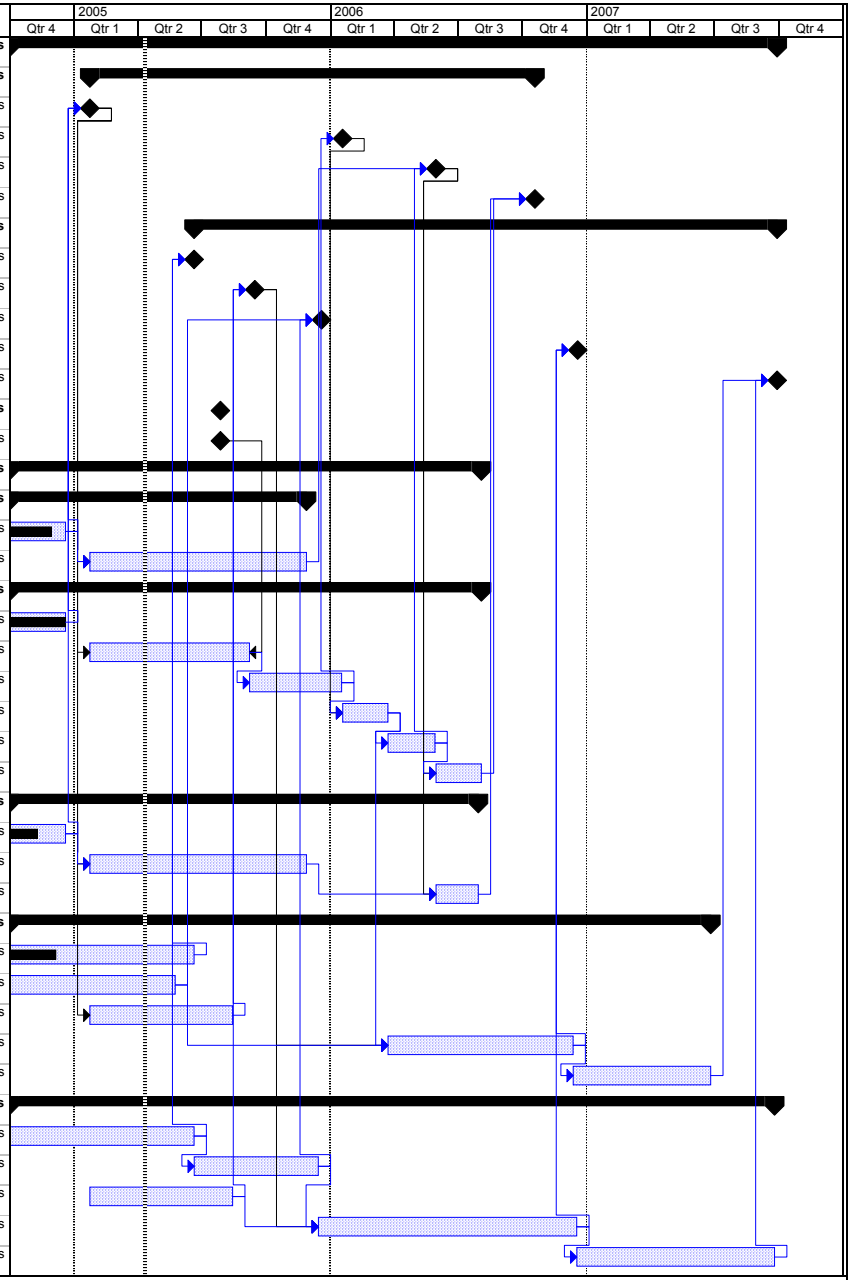

Project: VISTA Data Flow System
Saved: 11 Apr '05
File: \\vulcan\projects\Vista\WBS\20_dataflow\work_in_progress\vdfs_v2.mpp

Printed: 11 Apr '05 5:18 PM

Task | Milestone | Rolled Up Split | External Tasks | Deadline
Split | Summary | Rolled Up Milestone | Project Summary
Progress | Rolled Up Task | Rolled Up Progress | External Milestone
